Student "Kissing" Bridge Relocation Project
Fall Work Schedule
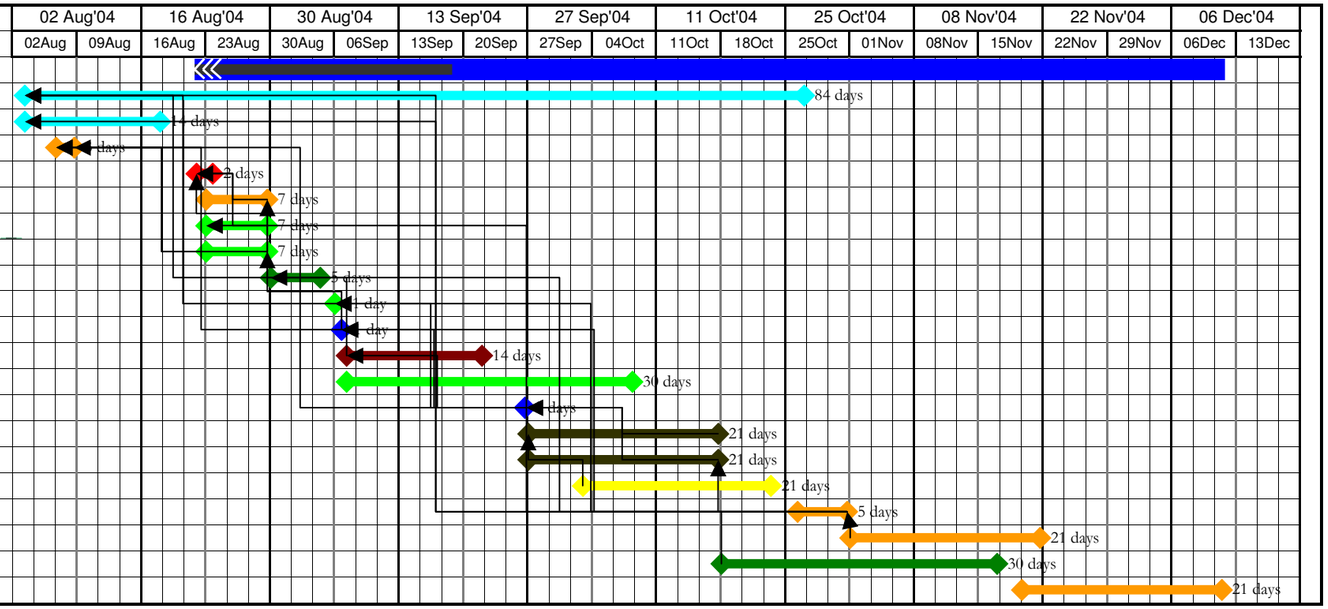
Duration	Project	%	Successor	Start	Finish
(days)	Project Duration	25		21-Aug-2004	10-Dec-2004
84	Order replacement bridge	0		03-Aug-2004	26-Oct-2004
14	Approve replacement shop drawings	0		03-Aug-2004	17-Aug-2004
3	Assemble, POUR, & STRIP East abutment	0		06-Aug-2004	08-Aug-2004
2	Return to campus	0		21-Aug-2004	23-Aug-2004
7	Repair damaged structural sections	0	8	22-Aug-2004	29-Aug-2004
7	Set replacement bearing plates	0	8	22-Aug-2004	29-Aug-2004
7	Set Student Bridge bearing plates	0	7,8	22-Aug-2004	29-Aug-2004
5	Remove trees at replacement site	0	5	30-Aug-2004	04-Sep-2004
1	Site demo for replacement (remove stairs, ect)	0	5	05-Sep-2004	06-Sep-2004
1	CUT & MOVE STUDENT BRIDGE	0	7FS,11SF	07-Sep-2004	07-Sep-2004
14	Blast, Repair, & Paint bridge	0	9SF	07-Sep-2004	21-Sep-2004
30	Order & install historical signs	0		07-Sep-2004	07-Oct-2004
5	SET BRIDGE ONTO NEW FOUNDATIONS	0	7FF, 13,14,15	21-Sep-2004	26-Sep-2004
21	Begin Anchorwall & earthwork, East	0	17FF	26-Sep-2004	17-Oct-2004
21	Begin Anchorwall & earthwork, West	0	17FF	26-Sep-2004	17-Oct-2004
21	Install lighting	0	18SS	02-Oct-2004	23-Oct-2004
5	SET REPLACEMENT BRIDGE	0	5,6,10,12,13,14,	26-Oct-2004	31-Oct-2004
21	Replacement site prep (sidewalks, access ramps, ect)	0	21SF	31-Oct-2004	21-Nov-2004
30	Landscaping	0	19SF	17-Oct-2004	16-Nov-2004
21	Project close out	0		19-Nov-2004	10-Dec-2004
